

# Marengo Valley Elementary Remodeling & Addition

Activity Report

August 14, 2017

**OBJECTIVE:**

RENOVATION AND ADDITION TO  
MARENGO VALLEY ELEMENTARY  
SCHOOL

**SCOPE:**

DESIGN AND CONSTRUCT FOR FALL  
2017 OCCUPANCY

KEITH HITLS  
DISTRICT ADMINISTRATOR  
715-682-7080  
KHILTS@SDAK.12.NET

**RECENT ACTIVITY:**





- 76% shop drawings submitted
- 76% shop drawings reviewed
- Installed topsoil and completed the trail west of playground.
- Installed brick on multi-purpose
- Installed casework and markerboards.
- Installed soffit in art room and finished entrance ceiling.
- Installed carpeting and flooring in Area B.
- Installed electrical fixtures in Area A.
- Installed roof drains and insulation

**CRITICAL UPCOMING EVENTS:**

- Finish brick at multi-purpose room.
- Finish casework, doors and hardware.
- Finish roofing.

**KEY DATES:**

- Next meeting - 8-17-17
- Punch list - 8-17-17

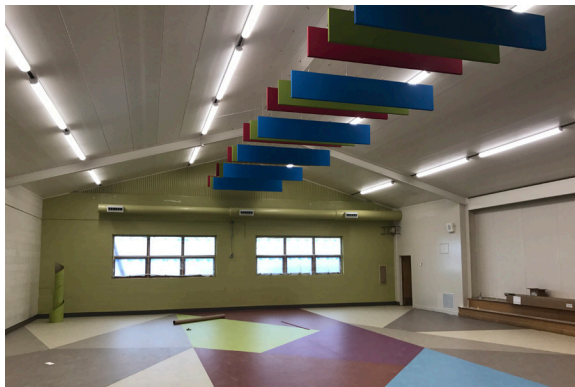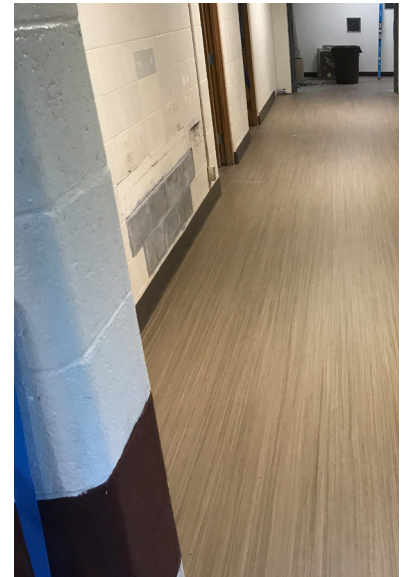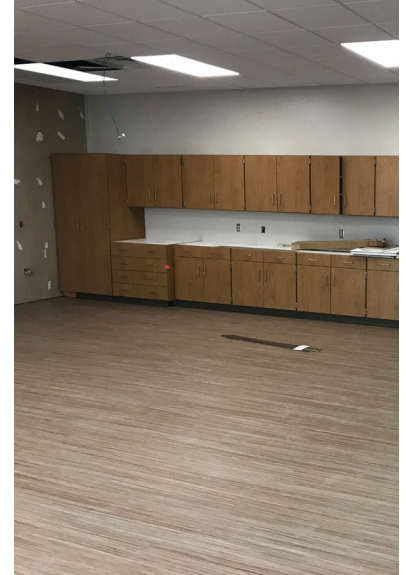

  
We are here
