

Lake Superior Elementary Remodeling & Additions

Activity Report

August 14, 2017

OBJECTIVE:

RENOVATION AND ADDITIONS
TO LAKE SUPERIOR ELEMENTARY
SCHOOL

SCOPE:

DESIGN AND CONSTRUCT FOR FALL
2017 OCCUPANCY

KEITH HILTS
DISTRICT ADMINISTRATOR
715-682-7080
KHILTS@SDAK.12.NET

RECENT ACTIVITY:


- 48% shop drawings submitted
- 48% shop drawings reviewed
- Installed cmu bearing walls and sidewalks in Area H.
- Finished radiant panel installations in ceilings.
- Installed electrical wiring and devices in Areas C, D and E.
- Installed door frames in Area H
- Installed ceiling tile in Areas D and G.
- Installed flooring in Area G.
- Started installing aluminum entrances.

CRITICAL UPCOMING EVENTS:

- Install bituminous paving.
- Install plumbing fixtures.
- Continue floor finishes.

KEY DATES:

- Next meeting 8-16-17
- Fire Alarm Test 8-14-17
- Furniture delivery 8-21-17

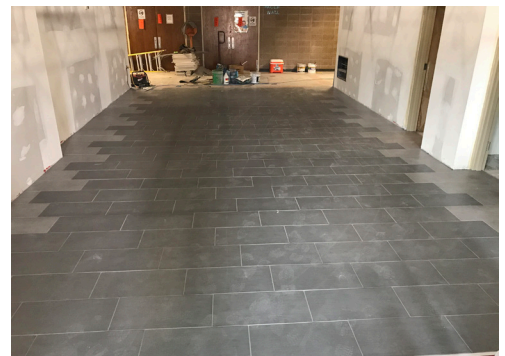

Construction: Phase I

Occupancy

Construction: Phase IA

Occupancy

Construction: Phase 2

Occupancy

4/2017

5/2017

6/2017

7/2017

8/2017

9/2017

10/2017

11/2017

↑
We are here
